



Building Progress Layout

SS 024

Saturday 16-June-2018

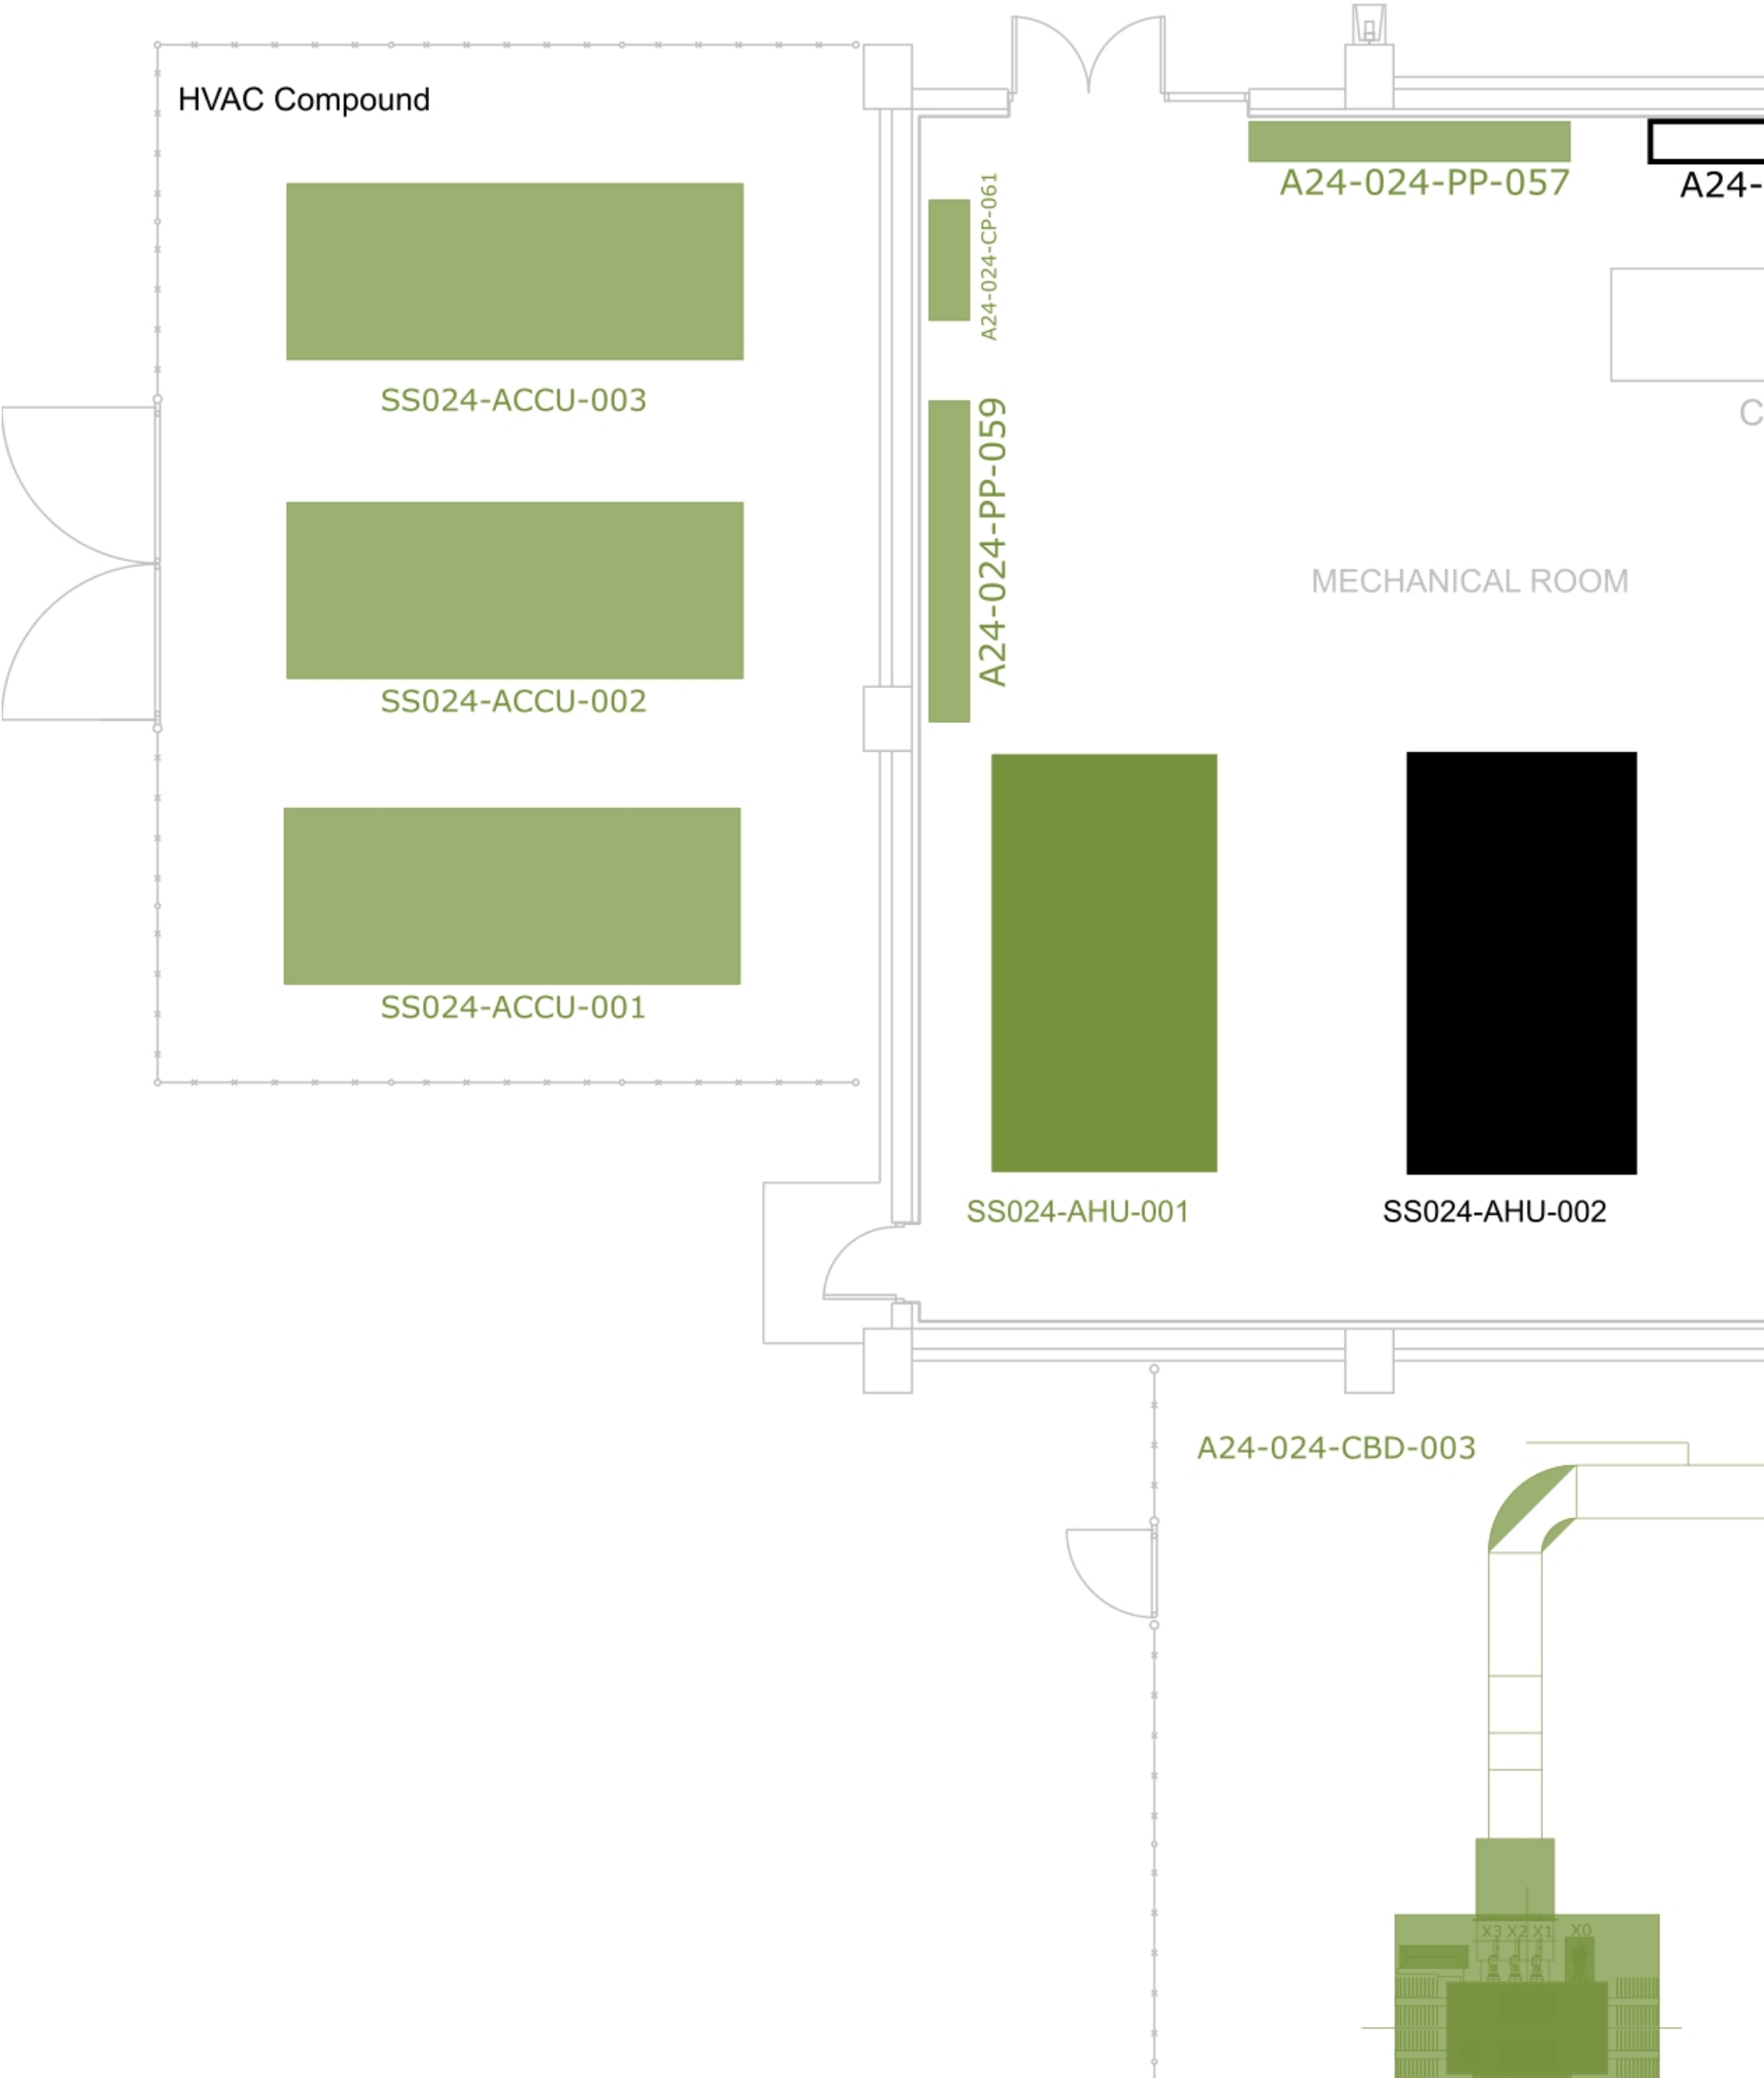

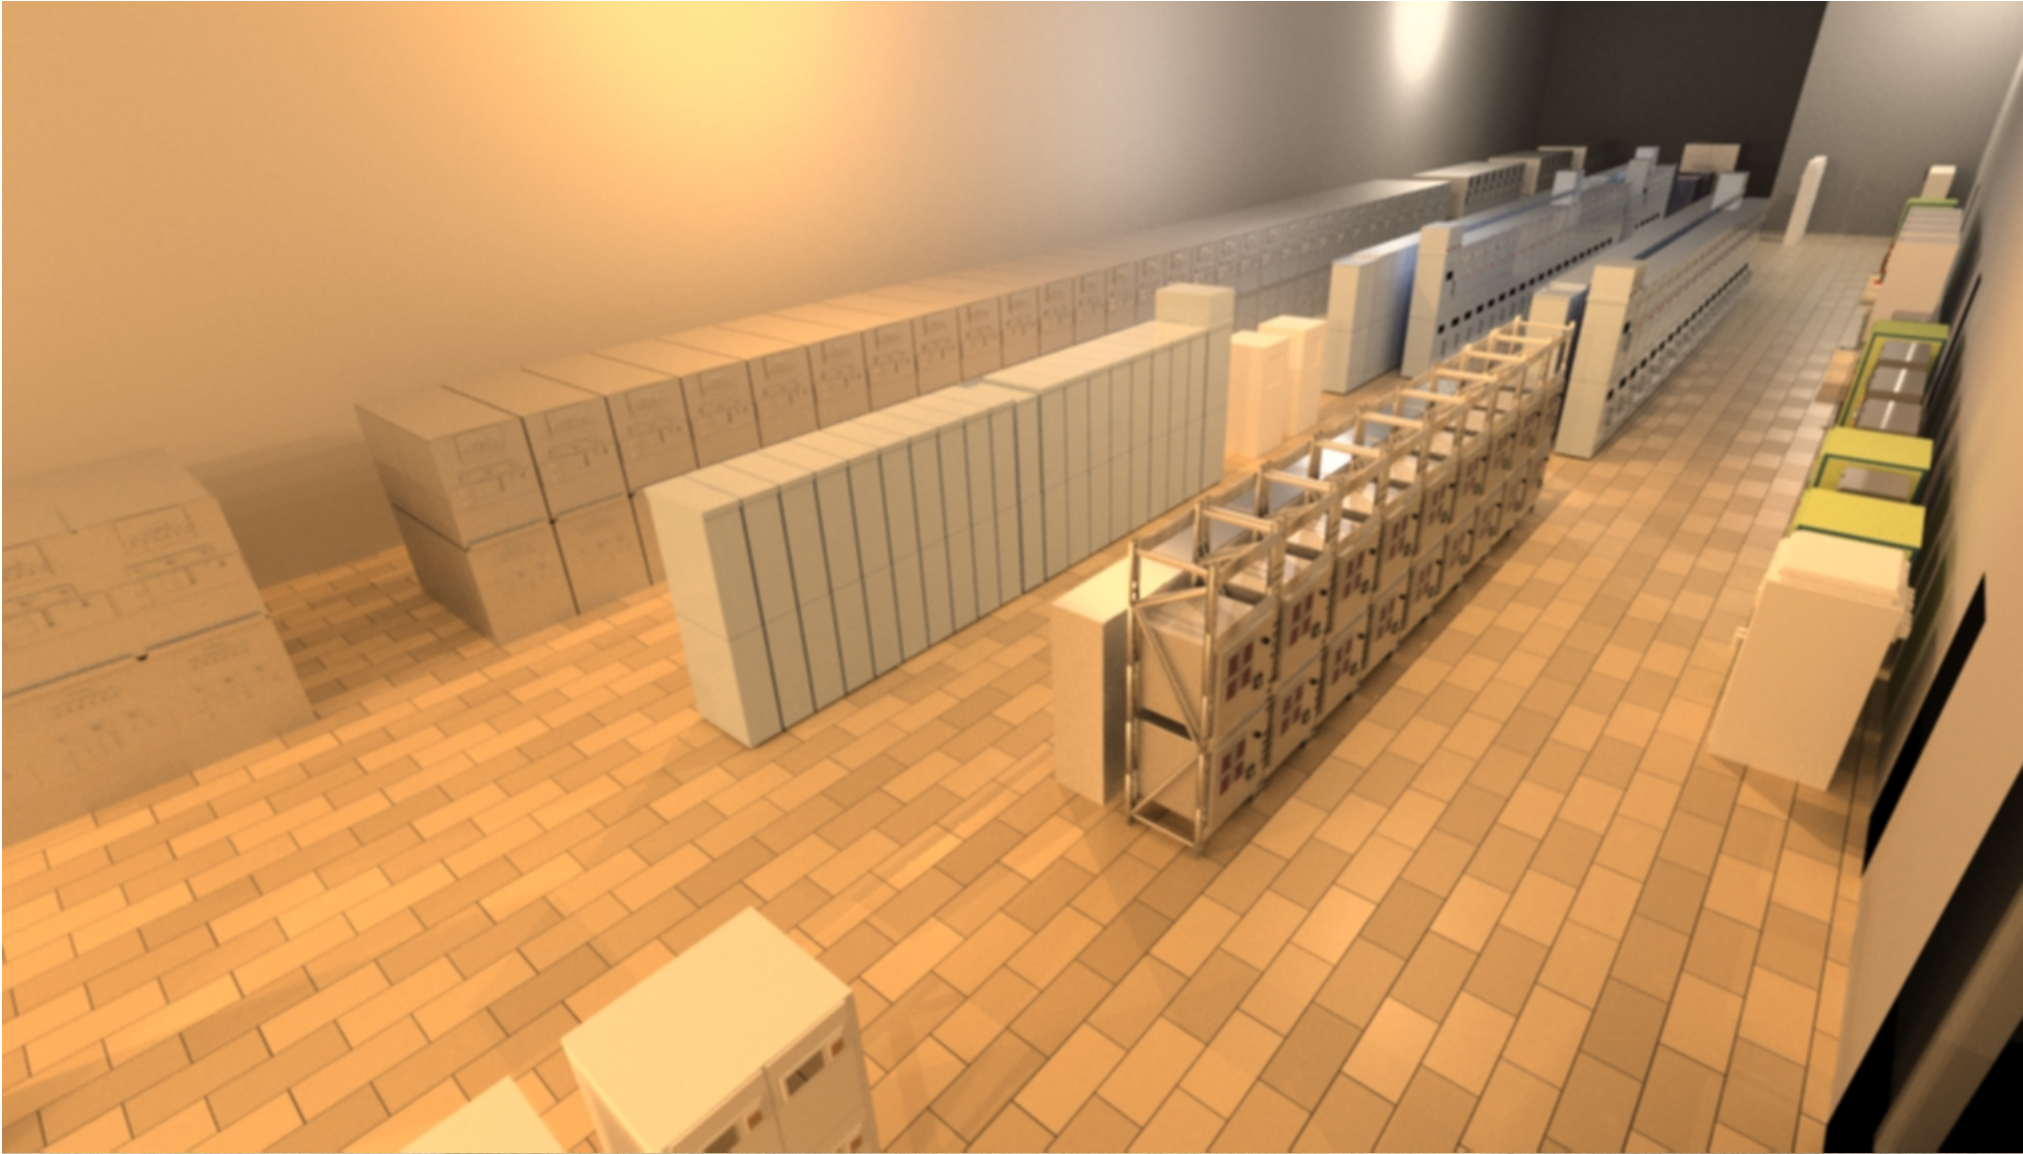

Unit	Type	Scope	Installed	Pending
A24	Battery	2	2	0
A24	Cable Bus	11	11	0
A24	HVAC	12	8	4
A24	MCC	8	8	0
A24	Misc	10	10	0

A24	Panel	33	33	0
A24	Switchgear	6	6	0
A24	Transformer	15	15	0
A24	VSD	16	16	0
TOTAL	TOTAL	113	109	4
